



Buru Energy Limited
ABN 71 130 651 437
Level 2, 97 William Street
Perth, Western Australia 6000
PO Box 7794, Perth
Cloisters Square WA 6850
Ph: 61-8 9215 1800
Fax: 61-8 9215 1899
www.buruenergy.com

ASX ANNOUNCEMENT (ASX: BRU) 12 July 2012

Weekly Drilling Progress Report – Ungani North-1

Buru Energy Limited (“**Buru**” or “**Company**”) provides the following weekly update on the drilling operations at the Ungani North-1 well as at 06:00hrs, 12 July 2012 (AWST).

Ungani North-1 is the fourth well to be drilled by the Buru – Mitsubishi Corporation (“**MC**”) Joint Venture in 2012. The well is located in exploration permit EP 391 some 100 kilometres to the east of Broome, and lies some six kilometres north of the Ungani Production Facility. Buru and MC each have a 50% interest in this well and in EP 391, with MC and Buru each contributing 50% of the cost of the well.

Since the initial progress report, the well was drilled ahead in 17½” hole to a measured depth of 624 metres and 13⅜” surface casing was run and cemented to 620 metres. As at 06:00 hours today, the well was being prepared to be drilled ahead in 12¼” hole to the intermediate casing point expected to be at a measured depth of 2,260 metres.

In accordance with its policy of releasing weekly drilling progress reports, the Company expects to issue a further drilling progress report on 19 July 2012, subject to any material events occurring in the meantime.

Further information on the Company is available at: www.buruenergy.com


For inquiries please contact:

Eric Streitberg	Executive Director
Telephone	+61 8 9215 1800
Freecall	1800 337 330
Email	ericstreitberg@buruenergy.com


UNGANI NORTH-1

PERMIT	The Ungani North-1 well is located in exploration permit EP 391 some 100 kilometres east of Broome. Maps showing the location of the well are set out below.
WELL LOCATION	Latitude: 17° 55' 58.5" S Easting: 517415m Longitude: 123° 09' 52.0" E Northing: 8017229m
BURU'S INTEREST	Buru Energy Limited holds a 50% interest in the well
DATE OF PROGRESS REPORT	06:00hrs, 12 July 2012 (AWST)
PROPOSED TOTAL DEPTH	3,000 metres
CURRENT DEPTH	624 metres
PROGNOSED TIME TO COMPLETION	32 days
SPUD DATE	5 July 2012
DAYS SINCE SPUD	7 days
CURRENT TARGET FORMATION	The Ungani North-1 well is targeting the Ungani Dolomite as seen in the Ungani Field together with the underlying Nullara section which had good oil and gas shows in the Ungani-1 well.
OPERATIONS SINCE LAST PROGRESS REPORT	Since the initial progress report, the well was drilled ahead in 17½" hole to a measured depth of 624 metres and 13¾" surface casing was run and cemented to 620 metres. As at 06:00 hours today, the well was being prepared to be drilled ahead in 12¼" hole.
HYDROCARBON INDICATIONS	None – None expected
FORWARD OPERATIONS	Drill ahead to the intermediate casing point expected to be at a measured depth of 2,260 metres.

LOCATION MAPS

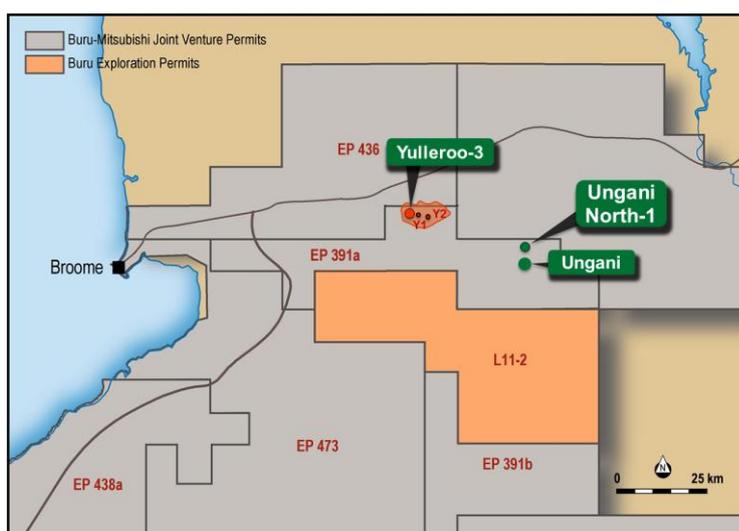

Ungani North-1 Regional location map

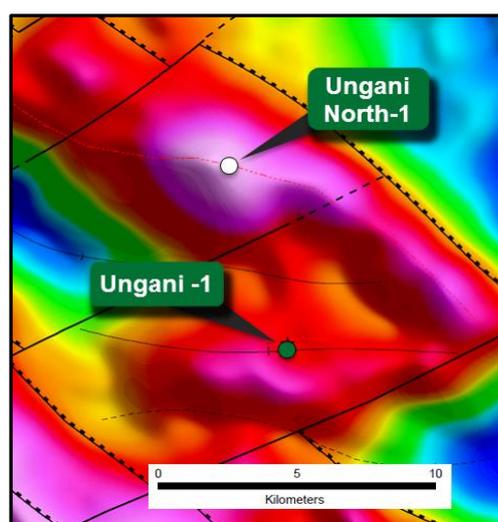

Ungani North-1 Interpreted gravity gradient map
